



ID		Task Name	Duration	Start	Finish	Predec	Resource Names	Sun 21 Oct	Mon 22 Oct
1	✓	Agile Team Meeting to review Project Plan, Review 3rd data load validation reports	0.5 days	Tue 23/10/07	Tue 23/10/07		Frank Siluk	S	M
2	✓	Provide data dump from SRVAGILE04 email to Doug Carnegie, Mike Superville, and Frank Siluk	0.25 days	Wed 24/10/07	Wed 24/10/07		Marc-Alexndre Belanger		
3	✓	Make necessary Modification in respect to Auto Numbering and verify no formatting errors exists on screens	3 days	Wed 24/10/07	Fri 26/10/07		Doug Carnegie		
4	✓	Review 3rd data load results and findings with Doug and Mike	0.25 days	Wed 24/10/07	Wed 24/10/07		Agile Team + Doug and Mike		
5	✓	Make sure Backups are working on All Agile Environments review with Mike SuperVille if Required	0.5 days	Wed 24/10/07	Wed 24/10/07		Marc-Alexndre Belanger		
6	✓	Provide Training and Transfer of knowledge to Eric Cholette of PPSS on creating a Data Dump, Running Backups, Installing the Software, Client, Server, Installing a new set of data from a data load.	0.5 days	Thu 25/10/07	Thu 25/10/07		Marc-Alexndre Belanger		
7	✓	Stop All Engineering Changes, ECO's, Hold Back any Pending Changes, Keep Track of What remains to be done. Communicate with Sub-Contractors, Contract Mfg's and Agile Team ** Manage emergencies manually outside of the system ** to be fixed in Agile later *	0.25 days	Thu 25/10/07	Thu 25/10/07		Samy Levy & Claude Brisson		
8	✓	A Full Backup of Positron, Pubsafe, Power All Databases will be taken Thursday nite at 8:00pm this will be the frozen period for Data	0.2 days	Thu 25/10/07	Thu 25/10/07		Ovidiu Plesa		
9	✓	Ovidiu and Deborah are to confirm by email the programming logic they are using to extract power and pss data, which data they are taking and where they are taking it from?	0.2 days	Thu 25/10/07	Thu 25/10/07		Deborah MacDonald and Ovidiu Plesa		
10	✓	The Full Backup taken of Positron, Pubsafe, Power All Databases will be restored in MFG Test environment Ovidiu will provide user logon and password instructions to get into MFG Test.	0.2 days	Fri 26/10/07	Fri 26/10/07		Ovidiu Plesa		
11	✓	Make two sets of Tapes for Archives	0.2 days	Fri 26/10/07	Fri 26/10/07		Ovidiu Plesa		
12	✓	Send Messages to User Community inform them that MFG Test is not to be used for other than Agile Validation	0.2 days	Fri 26/10/07	Fri 26/10/07		Ovidiu Plesa		

Project: AGILE GO LIVE TASKS REV Date: Mon 29/10/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID		Task Name	Duration	Start	Finish	Predec	Resource Names	Sun 21 Oct	Mon 22 Oct
13		Prepare System for Data Extract, Refresh Files, Master Bom Files, SUPER BOMS PPSS PRODUCTS , MISSINGSPARTS, DB8PARTS, Power-Products Master Boms including Engineering DB's	0.2 days	Fri 26/10/07	Fri 26/10/07		Deborah MacDonald and Ovidiu Plesa	S	M
14		Run Data Extracts Create (2) Two sets of Files A) Power & Common Part,Boms,AVL's, Mfg, etc. B) PPSS & Common Parts,Boms,AVL's,Mfg's etc. C) PPSS ; POWER and Common Complete Set NO LONGER REQUIRED STEP C REMOVED	0.2 days	Fri 26/10/07	Fri 26/10/07		Ovidiu Plesa		
15		Send Each of the Above Extract in separate Zipped Files to the Attention of Doug Carnegie, Mike Superville & Frank Siluk	0.2 days	Fri 26/10/07	Fri 26/10/07		Ovidiu Plesa		
16		J-Squared will confirm they received all required files and begin process of Data-Manipulation and Conversion to Agile data format	0.2 days	Fri 26/10/07	Fri 26/10/07		Mike SuperVille		
17		Once J-Square encounters certain errors or messages related to the Missing Sub-Classes a spreadsheet will be sent to Daniel Fortin and Adrian Nica for resolution.	0.2 days	Sat 27/10/07	Sat 27/10/07		Mike SuperVille		
18		Daniel Fortin and Adrian Nica will provide the answers to the Missing Sub-Classes and return them by email to Mike Superville for him to continue his process	0.2 days	Sat 27/10/07	Sat 27/10/07		Daniel Fortin and Adrian Nica		
19		A Conference call will be setup with a DIAL IN number by Frank Siluk to provide a status on Saturday at 12:00pm	0.2 days	Sat 27/10/07	Sat 27/10/07		Doug to Organize All Team Members to Call in.		
20		Estimated time for Positon to receive Agile Dataload Files = Sunday Morning ?? Time ?? (2) Two sets of files will be received as discribed in TASK 14 they will be emailed to Ovidiu Plesa, Marc Alexandre Belanger and Frank Siluk	0.5 days	Sun 28/10/07	Sun 28/10/07		Mike SuperVille		
21		Once the (2) Files sets are received Marc Alexandre Belanger will proceed to install PPSS's Data on SRVAgile04; Power's Data on SRVAgile05; and repeat the same steps for the VMWARE workstations SRVAgile 01 or 02	0.25 days	Sun 28/10/07	Sun 28/10/07		Marc Alexandre Belanger		
22		Once the new data is loaded on the producion servers Marc will inform the group by email	0.2 days	Sun 28/10/07	Sun 28/10/07		Marc-Alexndre Belanger		










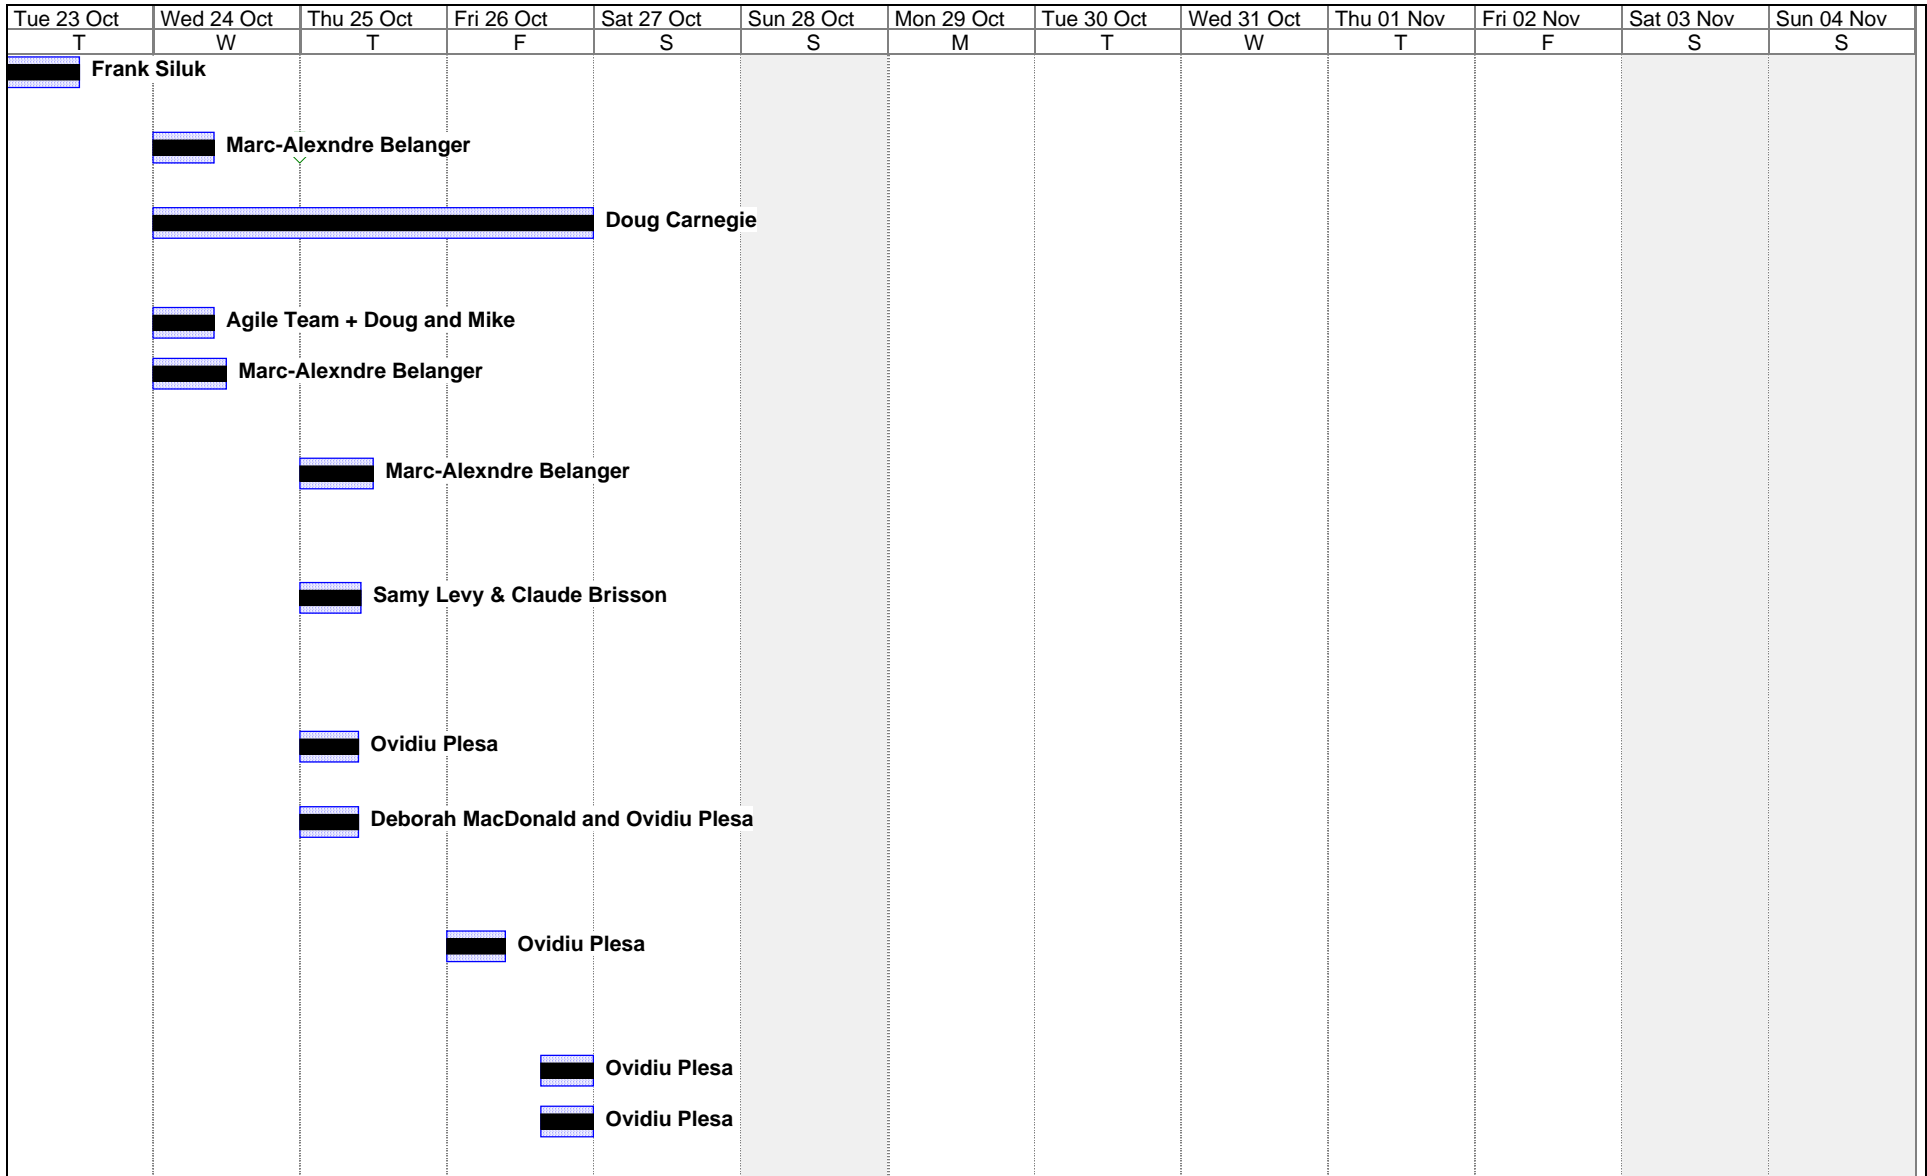


Project: AGILE GO LIVE TASKS REV Date: Mon 29/10/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	











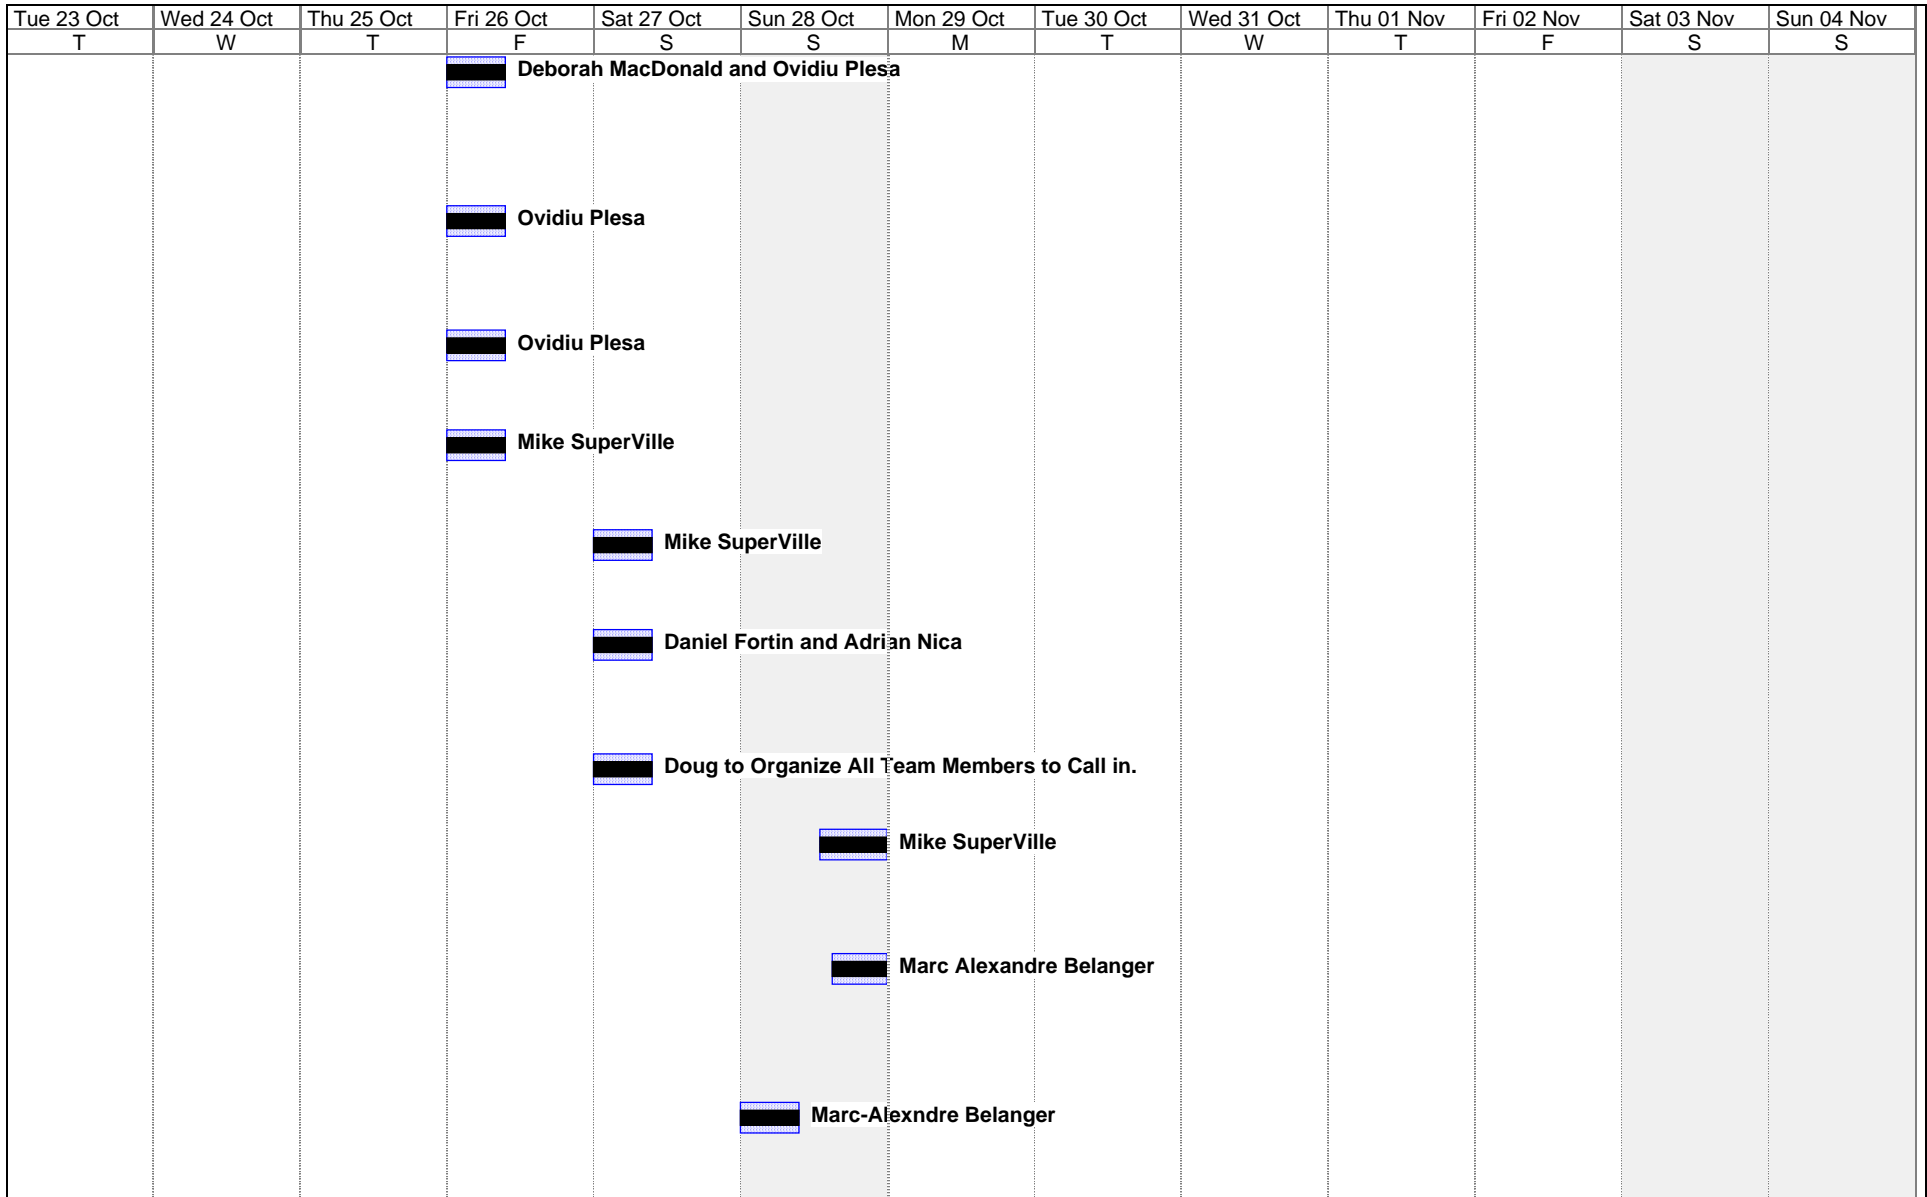

ID	Task Name	Duration	Start	Finish	Predec	Resource Names	Sun 21 Oct	Mon 22 Oct
23	Team will logon to either PPSS or Power Agile Server and perform a validation to ensure everything is correct and prepare a summary of their findings to be reviewed Monday by the complete Agile Team including consultants?	0.5 days	Sun 28/10/07	Sun 28/10/07		Adrian Nica, Daniel Fortin, Jeff Larivee, Louis Rene Beaudoin, Zaki Elayoubi, Claude Bisson, Samy Levy, Ovidiu Plesa, Donna Koussaya, Doug Carnegie, Mike Superville and Frank Siluk	S	M
24	Monday after a review of the findings, a decision will be taken to see if more time is Required ?? Tues Wed ?? Once this agreed to time is confirmed validation continues	0.5 days	Mon 29/10/07	Mon 29/10/07		Adrian Nica, Daniel Fortin, Jeff Larivee, Louis Rene Beaudoin, Zaki Elayoubi, Claude Bisson, Samy Levy, Ovidiu Plesa, Doug Carnegie, Mike Superville and Frank Siluk		
25	Once the agreed time has elapsed, a decision will be taken to GO Live or Not? If YES a signoff document will be completed if No an analysis of what needs to be resolved in order to go live.	0.1 days?	Wed 31/10/07	Wed 31/10/07		Adrian Nica, Daniel Fortin, Jeff Larivee, Louis Rene Beaudoin, Zaki Elayoubi, Claude Bisson, Samy Levy, Ovidiu Plesa, Doug		
26								
27	Entertain a Post Mortem 2 weeks from the GO Live Date ON November 12, 2007	0.2 days	Wed 14/11/07	Wed 14/11/07		Frank Siluk to Organize		




Project: AGILE GO LIVE TASKS REV Date: Mon 29/10/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	












Project: AGILE GO LIVE TASKS REV Date: Mon 29/10/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: AGILE GO LIVE TASKS REV Date: Mon 29/10/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

Tue 23 Oct	Wed 24 Oct	Thu 25 Oct	Fri 26 Oct	Sat 27 Oct	Sun 28 Oct	Mon 29 Oct	Tue 30 Oct	Wed 31 Oct	Thu 01 Nov	Fri 02 Nov	Sat 03 Nov	Sun 04 Nov
T	W	T	F	S	S	M	T	W	T	F	S	S
					 Adrian Nica, Daniel Fortin, Jeff Larivee, Louis Rene Beaudoin, Zaki Elayoubi, Claude Bisson, Samy Levy, Ovidi							
						 Adrian Nica, Daniel Fortin, Jeff Larivee, Louis Rene Beaudoin, Zaki Elayoubi, Claude Bisson, S						
								 Adrian Nica, Daniel Fortin, Jeff Larivee, Louis Rene Beaudoin, Zaki				

Project: AGILE GO LIVE TASKS REV Date: Mon 29/10/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	









Mon 05 Nov	Tue 06 Nov	Wed 07 Nov	Thu 08 Nov	Fri 09 Nov	Sat 10 Nov	Sun 11 Nov	Mon 12 Nov	Tue 13 Nov	Wed 14 Nov	Thu 15 Nov	Fri 16 Nov	Sat 17 Nov
M	T	W	T	F	S	S	M	T	W	T	F	S

Project: AGILE GO LIVE TASKS REV
Date: Mon 29/10/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Mon 05 Nov	Tue 06 Nov	Wed 07 Nov	Thu 08 Nov	Fri 09 Nov	Sat 10 Nov	Sun 11 Nov	Mon 12 Nov	Tue 13 Nov	Wed 14 Nov	Thu 15 Nov	Fri 16 Nov	Sat 17 Nov
M	T	W	T	F	S	S	M	T	W	T	F	S

Project: AGILE GO LIVE TASKS REV
Date: Mon 29/10/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
